

**Three Rivers
Community
Schools**

**Board Report
April 19, 2021**



The SKILLMAN Corporation
Project Administration
Construction Management

Three Rivers Community Schools

- High School – New Weight Room Addition
- Andrews/Norton Renovations
- Park/Ruth Hoppin Renovations



**Three Rivers
Community
Schools**

**Board Report
April 19, 2021**



The SKILLMAN Corporation
Project Administration
Construction Management

Table of Contents

- Work in Progress/Completed
- Progress Photos
- HS and Ruth Hoppin Site Logistics
- Four-Week Look Ahead
- Questions

**Three Rivers
Community
Schools**

**Board Report
April 19, 2021**



The SKILLMAN Corporation
Project Administration
Construction Management

Work in Progress / Completed

- Finalize Contracts
- Construction Scheduling
- Secure Permits
- Ruth Hoppin Abatement
- HS/MS Fiber Cable Relocated
- Submittals / Material Procurement
- Identify long lead time items.

Three Rivers
Community
Schools

Board Report
April 19, 2021



The **SKILLMAN** Corporation
Project Administration
Construction Management

Progress Photos



Ruth Hoppin Abatement

Three Rivers
Community
Schools

Board Report
April 19, 2021



The **SKILLMAN** Corporation
Project Administration
Construction Management

Progress Photos



Ruth Hoppin Abatement Interior

**Three Rivers
Community
Schools**

**Board Report
April 19, 2021**



The SKILLMAN Corporation
Project Administration
Construction Management

Progress Photos



Completed Ruth Hoppin Abatement


Three Rivers Community Schools

Board Report
April 19, 2021



The SKILLMAN Corporation
Project Administration
Construction Management

HS Site Logistics

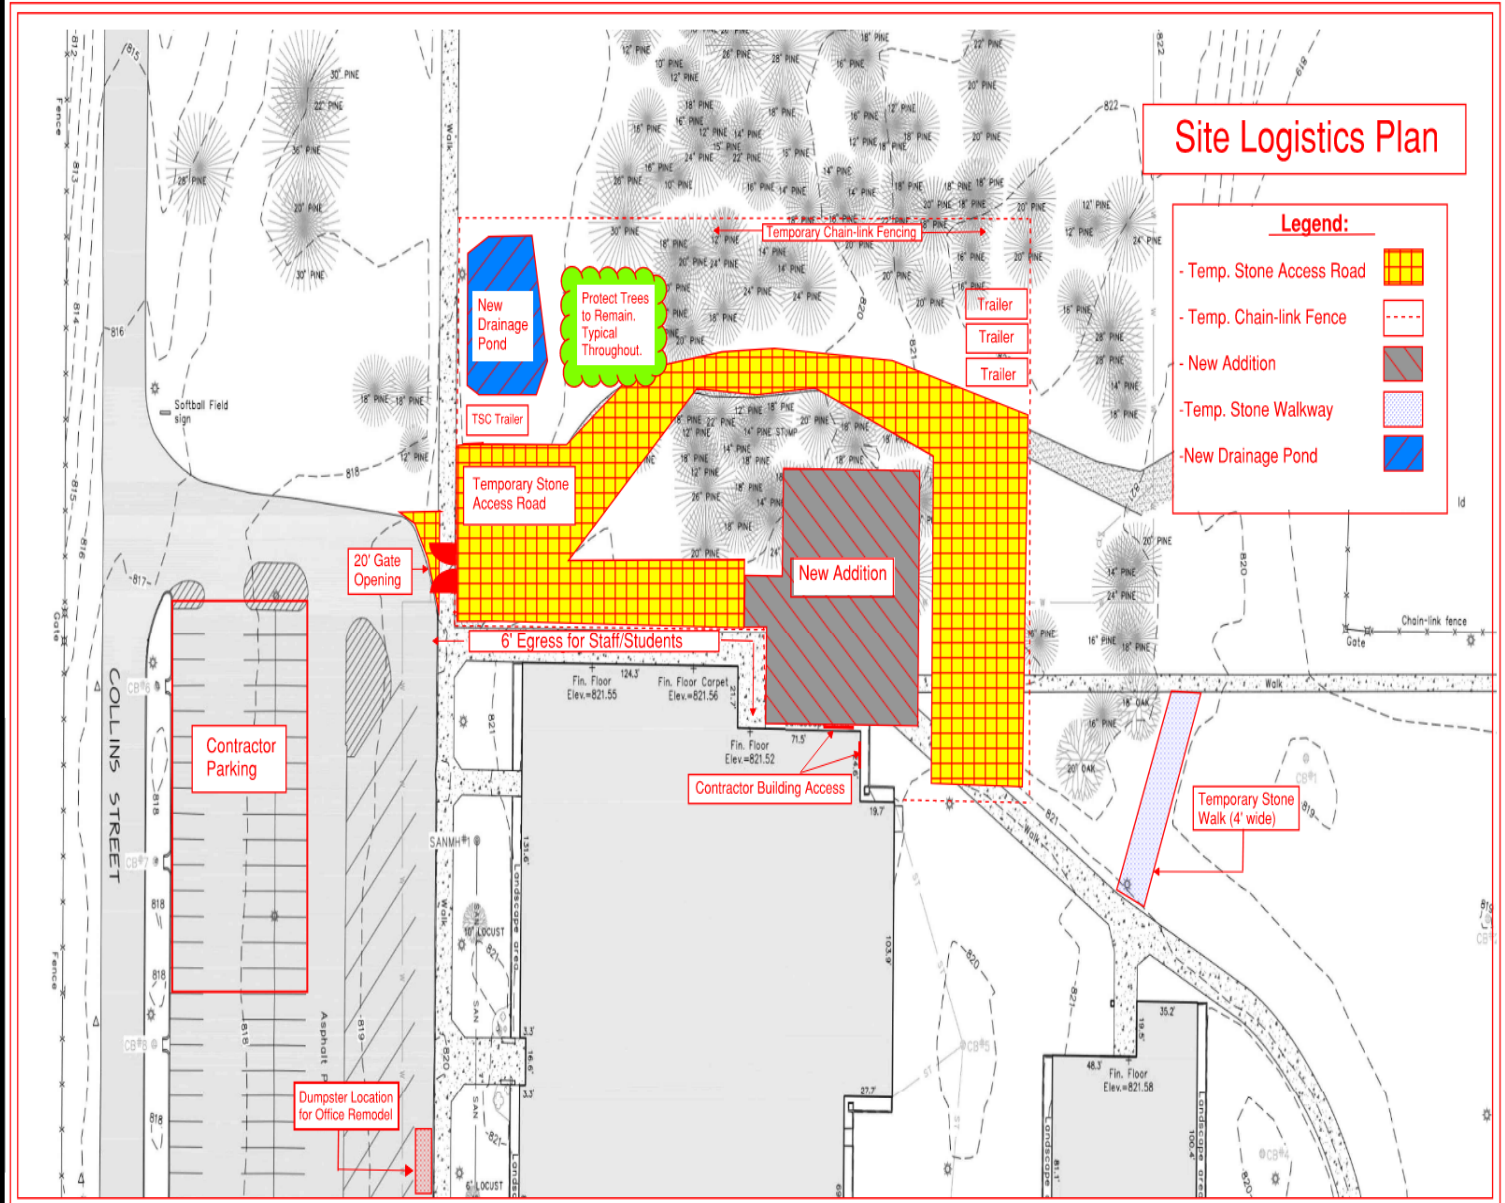


Three Rivers Community Schools - High School

Ruth Hoppin Site Logistics

Three Rivers
Community
Schools

Board Report
April 19, 2021

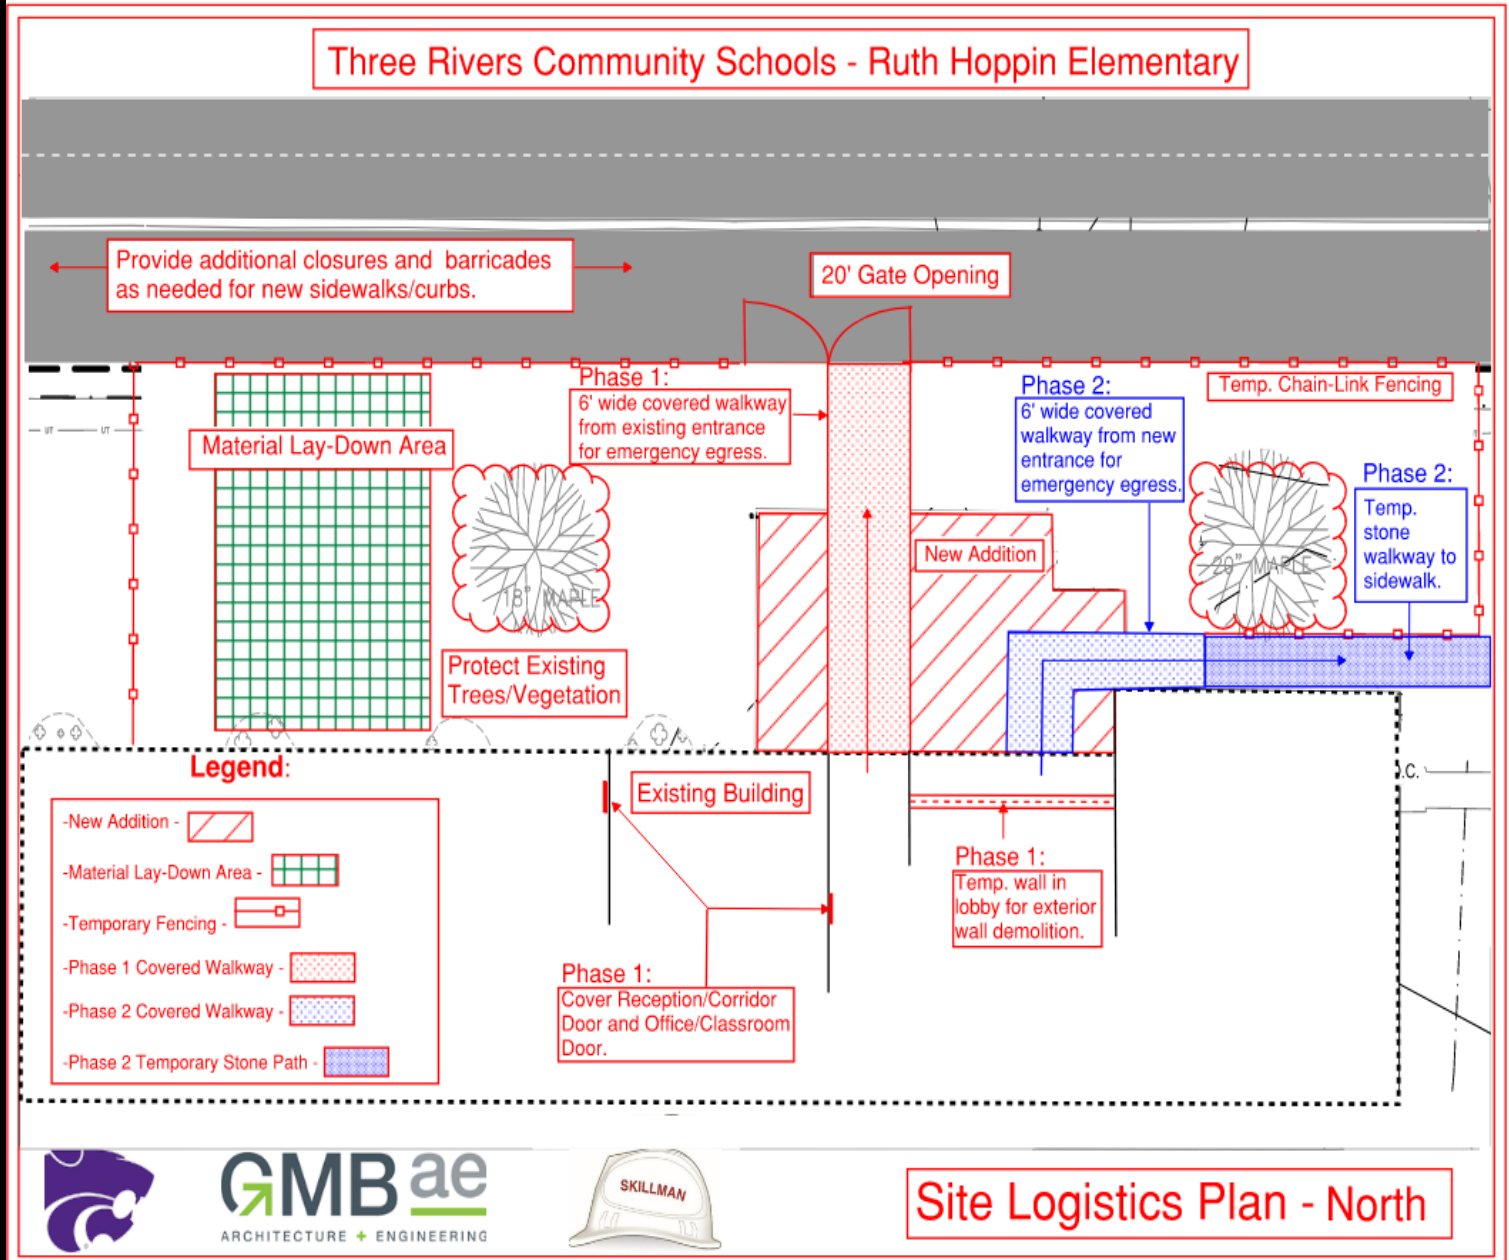

The SKILLMAN Corporation
Project Administration
Construction Management



GMBae
ARCHITECTURE + ENGINEERING



Four-Week Look Ahead

- Mobilize / Temp. Fencing at HS
- Site clearing and Building Pad prep. for HS Weight Room Addition.
- Mobilize / Temp. Fencing at Ruth Hoppin
- Install covered walkway for emergency egress and begin demolition/renovation of Ruth Hoppin Office Area.



**Three Rivers
Community
Schools**

**Board Report
April 19, 2021**



The SKILLMAN Corporation
Project Administration
Construction Management

Questions?
